

Capital Projects Update

...a report to Kill Devil Hills citizens of the status of projects currently under way. We'll usually update it every couple of weeks. Contact Steve Albright, Public Services Director, with any questions or comments at 480-4080 or steve@kdhnc.com.

Monday, March 8, 2021



Tentative **ROAD CLOSURES** and **WATER OUTAGES** (~ means "approximately"):

FULL Closure: E Dean St just west of Wrightsville Blvd, Wednesday, March 10, 8:00 a.m to 4:30 p.m.

PARTIAL Closure: Partial lane closures, pipe work on S Memorial Blvd just north of E Martin St Monday.

WATER OUTAGES: None.

2020/21 Streets Project: Fall Package - Cedar Drive, Captain's Lane, Teakwood Drive and Captain's Circle

Description: This project will provide pavement overlay for roads rated as in "Poor" condition, along with storm drainage improvements. Streets involved with the improvements include Cedar Drive, Captain's Lane, Teakwood Lane and Captain's Circle.

Start Date: Fall 2020

Finish Date: Spring 2021

Contractor: RPC Contracting, Inc.

Project Cost: Awarded: \$785,485

Recent Progress: Pipe deliveries have been made.

The next few days: Surveyors stake out for storm drainage; pipelaying is expected to start later this week, on Cedar Drive.



Map above shows roads included in project.

2020/21 Streets Project: Spring Package- Helga Street, Briggs Street, Fourth Street, East Martin Street, and East Dean Street

Description: This project will provide pavement overlay for roads rated as in "Poor" condition, along with storm drainage improvements. Streets involved with the improvements include East Helga Street, Briggs Street, East Fourth Street, East Martin Street, and East Dean Street.

Start Date: Fall 2020

Finish Date: Spring 2021

Contractor: RPC Contracting, Inc.

Project Cost: Awarded: \$632,685

Recent Progress: Storm drainage work is complete in the E Helga St / Briggs St area and NC 12 / Virginia Dare Trail near E Fourth Street; storm drain and utility adjustments in E Martin Street 98% complete. Concrete work completed in E Helga/Briggs area, except 1 driveway. First course of asphalt placed on E Helga and Briggs Streets.

The next few days: Storm drainage pipe and structure installation finishes E Martin St and moves to E Dean St, completing Spring Package storm drain work.

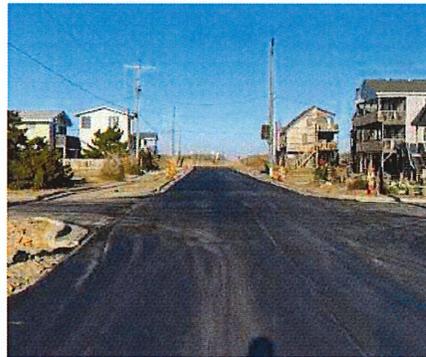


Photo looking east along East Helga Street, shows widening to 24' and first lift of asphalt. The block between Raymond Street and Virginia Dare Trail has curb & gutter, so the sidewalk may remain closer than 5' to the traveled way.



2021/22 Project: West Third Street and vicinity

Description: This project has 4 parts: (1) Street, sidewalk, drainage and water main work, W Third St (US 158 through Creek St). (2) Sidewalk, W Third St (Creek St to Bay Dr). (3) Street, drainage and water main work, Seminole St (W Third St to Indian St). (4) Replace drainage culverts, US 158 (W Third St through W Fifth St.)

Start Date: Fall 2021

Finish Date: Spring 2022

Contractor: not yet bid

Project Cost: approximately \$1.4 million

Recent Progress: Topographic surveying has been mostly completed. Preliminary engineering design is under way.

The next few days: Preliminary engineering design continues toward completion, followed by final design.

Map at right shows the 4 components of the project:

--- denotes Drainage only

— denotes street, drainage & water main

— denotes sidewalk & minimal drainage as needed to construct the sidewalk

